

# Wyomissing Area School District



## Facilities Workshop

Wednesday, February 16, 2022

Wyomissing Area Junior Senior High School  
Community Board Room


*“Inspiring Excellence, One Spartan at a Time”*

# Agenda:

- JSHS Construction Update
- WHEC Construction Update
- WREC Construction Update
- JSHS/WHEC/WREC Change Orders
- WHEC Crosswalk Update/Change Orders
- WHEC Gym Floor
- Capital Project Review

# JSHS Construction Update

- 400 hallway classrooms substantially completed.
- Old gym locker rooms and bathrooms are under construction.
- Transportation area is still under construction.
- Spring 2022- Old Gym, Field House, Nurses Suite upgrades and renovations.

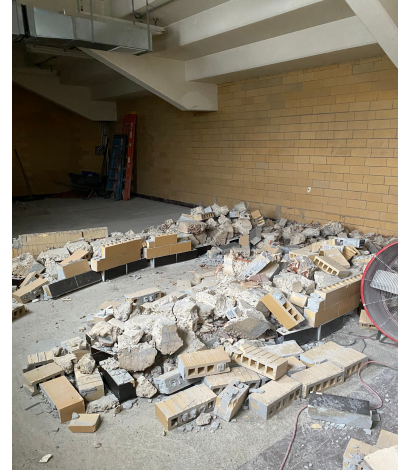

# WHEC Construction Update

- New Construction is scheduled to be completed in March.
- Once the new classrooms are completed, the existing classrooms will start being renovated.



# WHEC Crosswalk Update

- Crosswalk is complete.
- Project came in under budget
- Two small change orders due to Penndot requirements after the project was bid.
- Original Contract - \$73,895.00
- Final Pay App - \$69,856.67



# WHEC Gym Floor

- The Gym floor was damaged from a rain storm and after an investigation from our insurance company it was determined it was to be covered by our property insurance.
- Insurance company approved replacing the entire floor over the summer.

